



Salt River Pima-Maricopa Indian Community

10005 East Osborn Road • Scottsdale, Arizona 85256

Phone (480) 362-7700 • Fax (480) 362-5597

MONTHLY PROJECT PROGRESS UPDATE

Project: ECEC Classroom and Parking Expansion

Issued Date: July 5, 2023 | **July-2023 UPDATE**

Distribution:

	Name	Department/ Company
X	Tami Brungard	ECEC – Edu Leader
X	Lekisha Morris	ECEC
X	Barbara White	ECEC
X	Melody Herne	Act. Superintendent
X	Tate Walker	Public Relations Dir.
X	Deanna Scabby	Edu. Board./ Council
X	Mikah Carlos	Community Council

	Name	Department/ Company
X	Kimberly Manuel	ECEC – Policy Council
X	Carmen Briones	ECEC – Policy Council
X	Jennifer Correa	ECEC – Policy Council
X	Brittany Barranca	ECEC – Policy Council
X	Frank Perez	ECEC – Policy Council
X	Rene Uriarte	ECEC – Policy Council
X	Symone Kann	ECEC – Policy Council
X	Felicia Toya	ECEC – Policy Council

Work Completed:

Items



1. Parking lot asphalt pavement.
2. Building B Addition 1st floor concrete slab.
3. Building B Addition CMU vertical walls up to 2nd floor level.
4. Central Plant mechanical yard construction site work and footings.

Work anticipated in the next month:

1. First (4) Classroom (A146, A147, B147 & C115) renovations are scheduled to start 7/19.
2. Building B Addition CMU vertical walls continuation.
3. Central Plant mechanical yard concrete slab and CMU wall construction to start.
4. Infant playground areas renovation work to start.
5. New parking irrigation lines, decomposed granite and rip rap install.
6. New door install at exiting wall demo locations for laundry room access.

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Project Schedule | Three Week Look Ahead

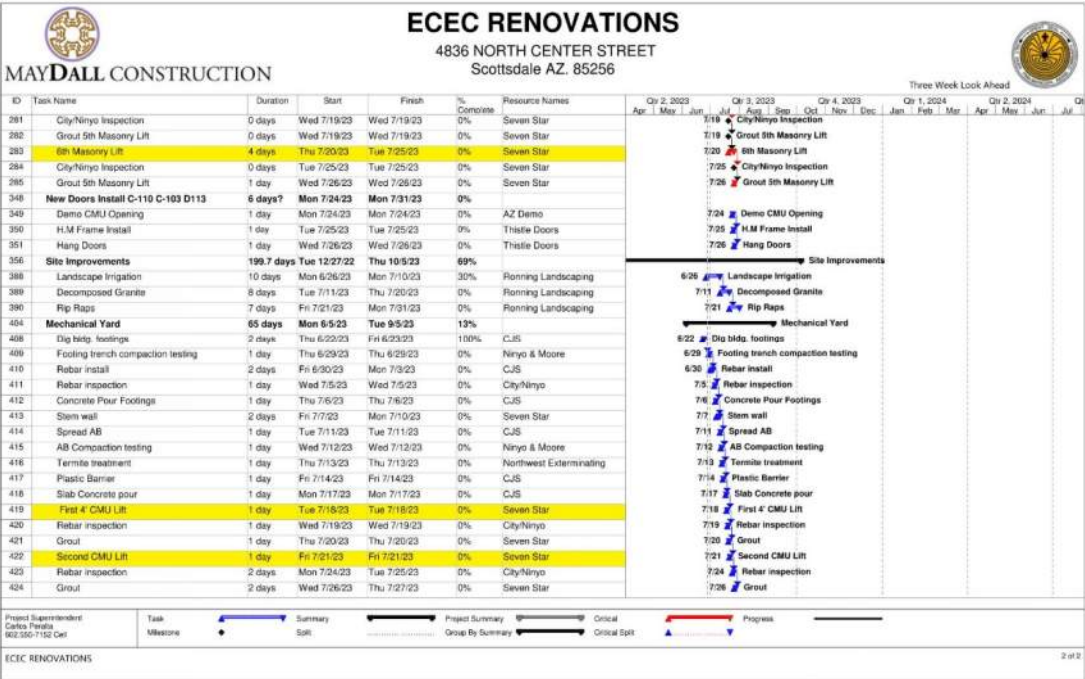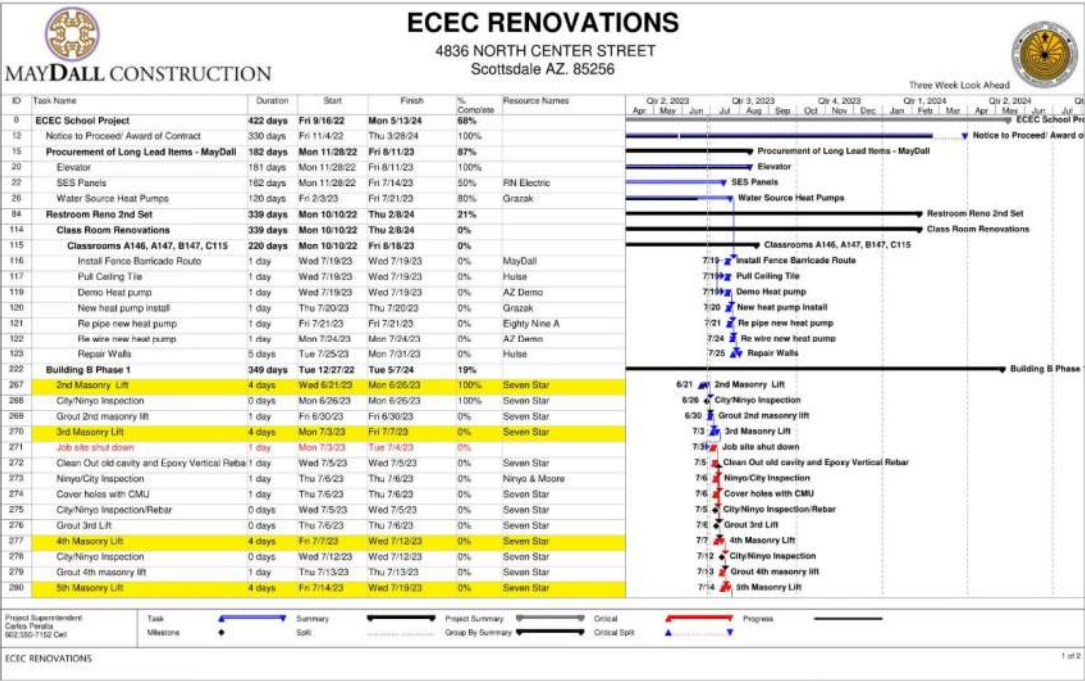


SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Progress Photos:

See attached.



Description

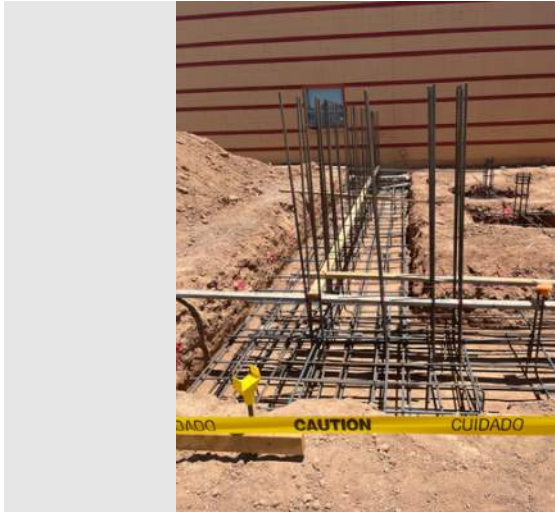

Description

Taken Date

06/30/2023 at 12:22 pm

Uploaded By


Carlos Peralta

Upload Date

06/30/2023 at 12:23 pm

File Name

D1F8E944-03D2-404B-8B0F-6FFC...

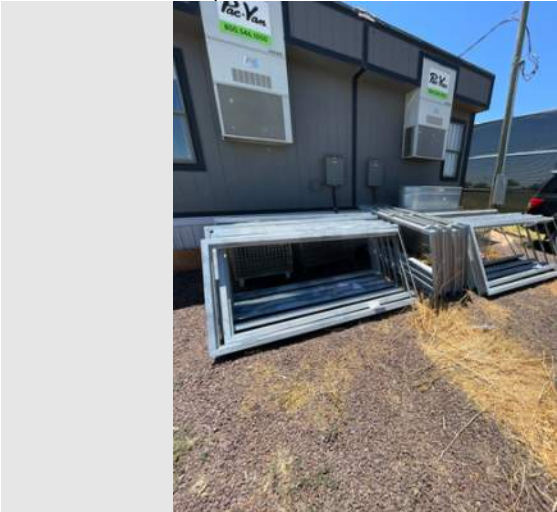

Description

Taken Date

06/30/2023 at 12:22 pm

Uploaded By

Carlos Peralta

Upload Date

06/30/2023 at 12:23 pm

File Name

451494CF-8CCC-43A8-8009-7FE9...



Description

Irrigation line at Islands and drip system.

Taken Date

06/30/2023 at 11:47 am

Uploaded By

Carlos Peralta

Upload Date

06/30/2023 at 11:47 am

File Name

7EF34787-EF06-4F5A-97DE-B659...

Taken Date

06/29/2023 at 01:19 pm

Uploaded By

Carlos Peralta

Upload Date

06/29/2023 at 01:19 pm

File Name

A9E53A04-ADC0-4A97-AB47-586...



Description

Ronning landscaping Materials at parking lot.

Taken Date

06/29/2023 at 01:19 pm

Uploaded By


Carlos Peralta

Upload Date

06/29/2023 at 01:19 pm

File Name

[B8BF7CF9-220C-411C-82D8-908...](#)

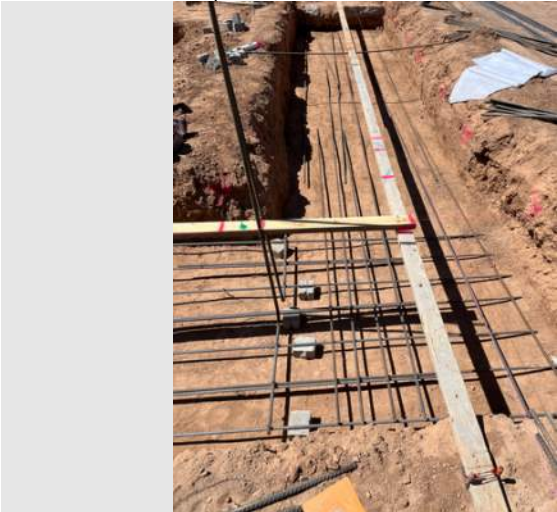

Description

Mechanical yard footing steel placement in progress

Taken Date

06/29/2023 at 10:11 am

Uploaded By

Carlos Peralta

Upload Date

06/29/2023 at 10:12 am

File Name

[C67ACD77-5385-42D2-97FD-996...](#)



Description

Taken Date

06/29/2023 at 10:13 am

Uploaded By


Carlos Peralta

Upload Date

06/29/2023 at 10:13 am

File Name

[8598203D-614A-46F1-B9D6-D6F...](#)

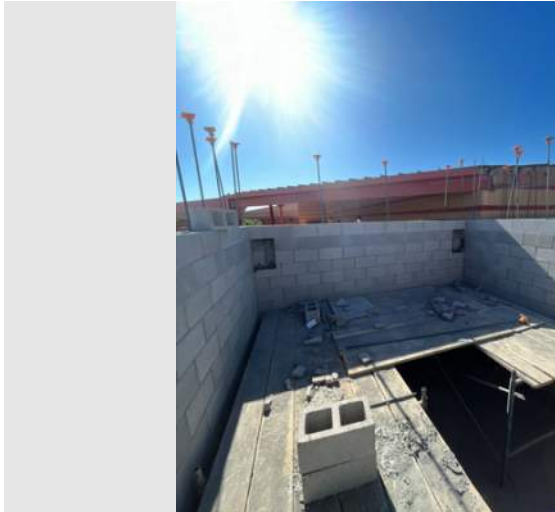

Description

East stairwells stringer pockets and embeds install in place

Taken Date

06/29/2023 at 08:28 am

Uploaded By

Carlos Peralta

Upload Date

06/29/2023 at 08:29 am

File Name

[F2CFEFD-9AFF-4361-B6BF-AC7C...](#)



Description

New cooling tower pedestals dug out and ready for steel.

Taken Date

06/28/2023 at 11:28 am

Uploaded By

Carlos Peralta

Upload Date

06/28/2023 at 11:29 am

File Name

[F5320316-8B64-4CA9-BF0F-FA55...](#)



Description

Elevator Beam joist on site.

Taken Date

06/28/2023 at 09:36 am

Uploaded By


Carlos Peralta

Upload Date

06/28/2023 at 09:36 am

File Name

[58FA013B-28C9-4A89-B873-15DE...](#)

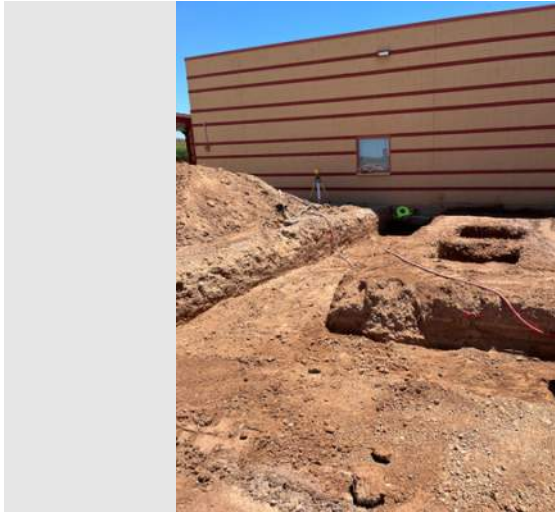

Description

Ready for Compaction inspection at mechanical yard.

Taken Date

06/28/2023 at 11:28 am

Uploaded By

Carlos Peralta

Upload Date

06/28/2023 at 11:28 am

File Name

[CF93FD95-670A-4744-8247-492...](#)



Description

Irrigation line.

Taken Date

06/28/2023 at 06:38 am

Uploaded By

Carlos Peralta

Upload Date

06/28/2023 at 06:38 am

File Name

[E4345A92-0DC8-435D-8BC8-888...](#)



Description

Irrigation lines and drip system running East and west at main retention.

Taken Date

06/28/2023 at 06:38 am

Uploaded By

Carlos Peralta

Upload Date

06/28/2023 at 06:47 am

File Name

56EE0A6E-B298-472E-AAF7-8E5A...



Description

Storm drain pipe under excysting footing.

Taken Date

06/27/2023 at 09:30 am

Uploaded By

Carlos Peralta

Upload Date

06/27/2023 at 09:34 am

File Name

F0587912-185B-4709-B3B5-1CA...



Description

Irrigation lines install in progress. Paring lot area.

Taken Date

06/28/2023 at 06:35 am

Uploaded By

Carlos Peralta

Upload Date

06/28/2023 at 06:35 am

File Name

0AC7B250-532B-419A-93A4-BCC...



Description

Storm drain pipe towards retention.

Taken Date

06/27/2023 at 09:29 am

Uploaded By

Carlos Peralta

Upload Date

06/27/2023 at 09:29 am

File Name

EE363915-BE75-42BE-851D-31E5...



Description

Green marking at new storage bldg.

Taken Date

06/27/2023 at 09:29 am

Uploaded By

Carlos Peralta

Upload Date

06/27/2023 at 09:29 am

File Name

[B7EE0554-75CE-4B3F-8709-38A...](#)



Description

Electrical sleeve for bldg. B

Taken Date

06/26/2023 at 07:16 am

Uploaded By

Carlos Peralta

Upload Date

06/26/2023 at 07:27 am

File Name

[644323C7-12E4-4790-BF0D-70AF...](#)



Description

Irrigation pipe on site.

Taken Date

06/26/2023 at 09:17 am

Uploaded By


Carlos Peralta

Upload Date

06/26/2023 at 09:17 am

File Name

[2A7BD220-8C03-42F2-A9A2-9EE...](#)

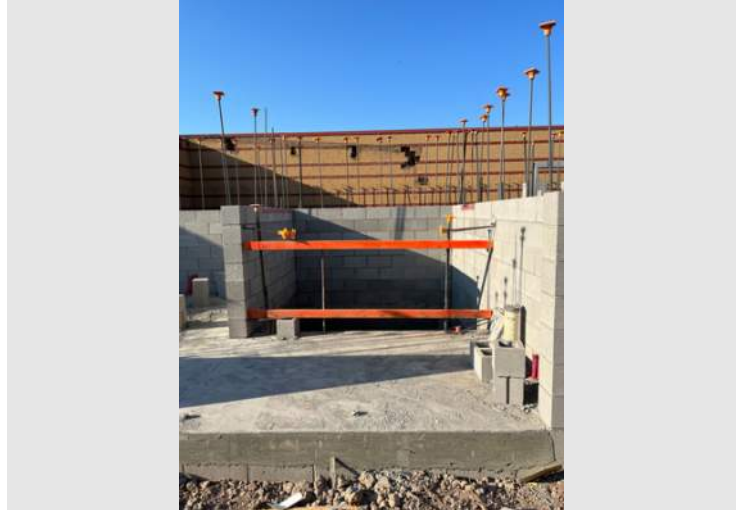

Description

Safety Barricade elevator shaft.

Taken Date

06/26/2023 at 07:05 am

Uploaded By


Carlos Peralta

Upload Date

06/26/2023 at 07:05 am

File Name

[F9C12EE5-74BC-48EC-97A1-7665...](#)

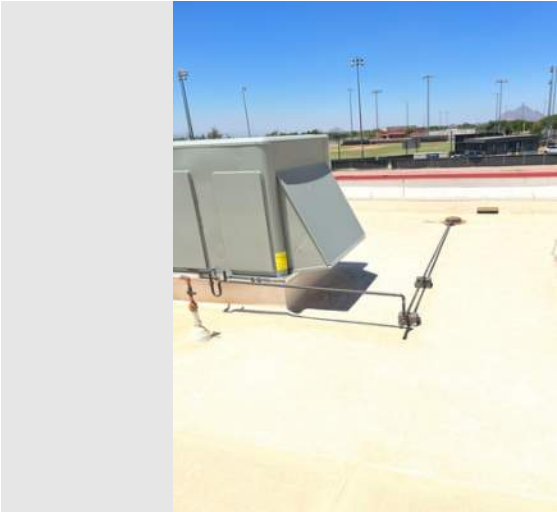

Description

Taken Date

06/22/2023 at 11:34 am

Uploaded By

Carlos Peralta

Upload Date

06/22/2023 at 11:37 am

File Name

[22E95B45-CA79-474D-8C8E-83A...](#)



Description

Taken Date

06/22/2023 at 11:27 am

Uploaded By

Carlos Peralta

Upload Date

06/22/2023 at 11:27 am

File Name

[61C581D9-40DF-4B47-B0A5-2FB...](#)



Description

Taken Date

06/22/2023 at 11:34 am

Uploaded By

Carlos Peralta

Upload Date

06/22/2023 at 11:34 am

File Name

[2310B990-142D-486D-8BD2-B74...](#)



Description

Taken Date

06/22/2023 at 11:26 am

Uploaded By

Carlos Peralta

Upload Date

06/22/2023 at 11:26 am

File Name

[3F6717FE-E90F-43A4-BF92-62B4...](#)



Description

Taken Date

06/20/2023 at 11:46 am

Uploaded By

Carlos Peralta

Upload Date

06/20/2023 at 12:41 pm

File Name

4CFF51C8-7F19-4480-953F-19F8...



Description

Door frames installed.

Taken Date

06/19/2023 at 11:52 am

Uploaded By

Carlos Peralta

Upload Date

06/19/2023 at 11:52 am

File Name

8A1DD71C-0F0B-4E65-AEF3-C7C...



Description

Mason starting on elevator shaft.

Taken Date

06/19/2023 at 11:52 am

Uploaded By

Carlos Peralta

Upload Date

06/19/2023 at 11:52 am

File Name

DA26504F-B552-48DC-9CA6-B84...



Description

South side doors installed.

Taken Date

06/19/2023 at 11:51 am

Uploaded By

Carlos Peralta

Upload Date

06/19/2023 at 11:52 am

File Name

E6267FE8-FE08-4B9F-A2FD-22CE...



Description

Inside the classroom window infill complete

Taken Date

06/16/2023 at 12:45 pm

Uploaded By

Carlos Peralta

Upload Date

06/16/2023 at 12:58 pm

File Name

[E881D906-18AD-48C1-8EBF-C76...](#)



Description

Existing window frame Removed

Taken Date

06/16/2023 at 10:47 am

Uploaded By


Carlos Peralta

Upload Date

06/16/2023 at 10:47 am

File Name

[8F53CB56-8FF1-41FC-9937-3890...](#)

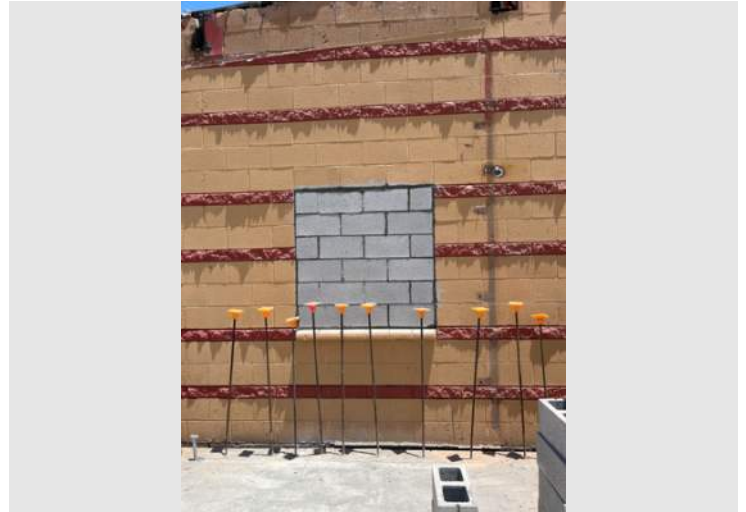

Description

Existing window at classroom infill complete

Taken Date

06/16/2023 at 12:45 pm

Uploaded By

Carlos Peralta

Upload Date

06/16/2023 at 12:45 pm

File Name

[F0F87D92-FD50-46D7-A27E-D3A...](#)



Description

Old lines been fed from SES to old storage Room.

Taken Date

06/14/2023 at 11:49 am

Uploaded By

Carlos Peralta

Upload Date

06/14/2023 at 11:50 am

File Name

[F144B0A1-57BF-477C-8786-52FB...](#)



Description

Underground electrical line from SES to old storage room.

Taken Date

06/14/2023 at 11:47 am

Uploaded By

Carlos Peralta

Upload Date

06/14/2023 at 11:47 am

File Name

[883D5E11-EFF9-423D-807B-BEE1...](#)



Description

Storm line running East to west.

Taken Date

06/14/2023 at 11:46 am

Uploaded By

Carlos Peralta

Upload Date

06/14/2023 at 11:46 am

File Name

[1F1A9A88-5DDF-44EA-8C88-AFB...](#)



Description

Storm drain T to retention pond.

Taken Date

06/14/2023 at 11:46 am

Uploaded By

Carlos Peralta

Upload Date

06/14/2023 at 11:47 am

File Name

[73EF3A5D-0A61-43AC-A314-D0B...](#)



Description

Old conduit for Conex.

Taken Date

06/14/2023 at 11:45 am

Uploaded By

Carlos Peralta

Upload Date

06/14/2023 at 11:46 am

File Name

[58E02885-6358-4A28-8D88-EC5...](#)



Description

Power lines north to south.

Taken Date

06/14/2023 at 11:45 am

Uploaded By


Carlos Peralta

Upload Date

06/14/2023 at 11:46 am

File Name

[88BDD2C7-691D-4536-8F3B-04E...](#)

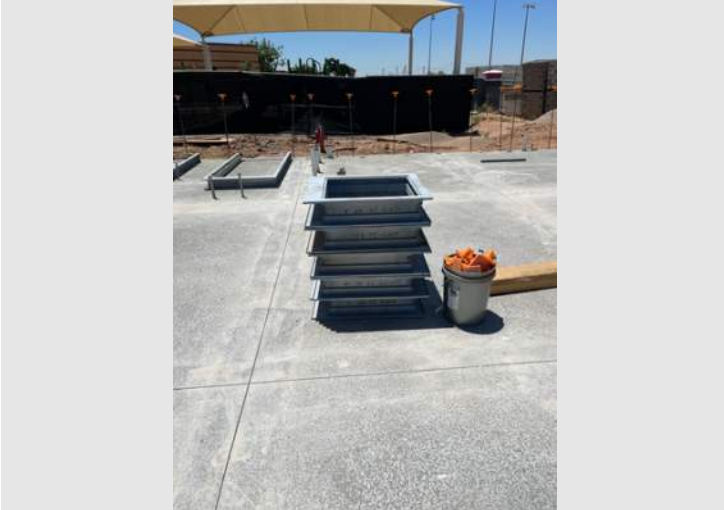

Description

First floor window frames

Taken Date

06/14/2023 at 11:42 am

Uploaded By

Carlos Peralta

Upload Date

06/14/2023 at 11:43 am

File Name

[D8A7F31C-0EB1-4799-B973-DEA...](#)



Description

Private blue stake complete.

Taken Date

06/14/2023 at 11:44 am

Uploaded By


Carlos Peralta

Upload Date

06/14/2023 at 11:46 am

File Name

[AA7E52C0-1A13-4CD5-B1D7-532...](#)

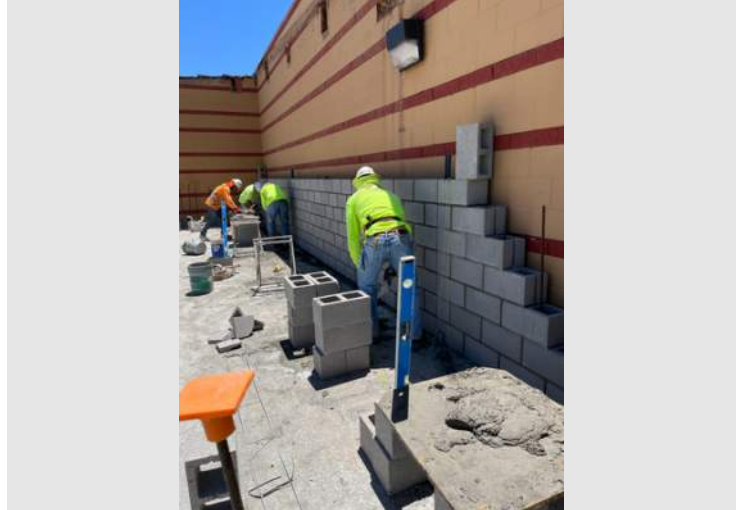

Description

South side bldg.. block first lift.

Taken Date

06/14/2023 at 11:42 am

Uploaded By

Carlos Peralta

Upload Date

06/14/2023 at 11:42 am

File Name

[5E1A9345-D1E1-49A8-9A14-833...](#)



Description

East Parking lot entry complete.

Taken Date

06/14/2023 at 10:17 am

Uploaded By


Carlos Peralta

Upload Date

06/14/2023 at 10:17 am

File Name

0FFD3E91-E0E6-48D6-A0F2-5B5A...

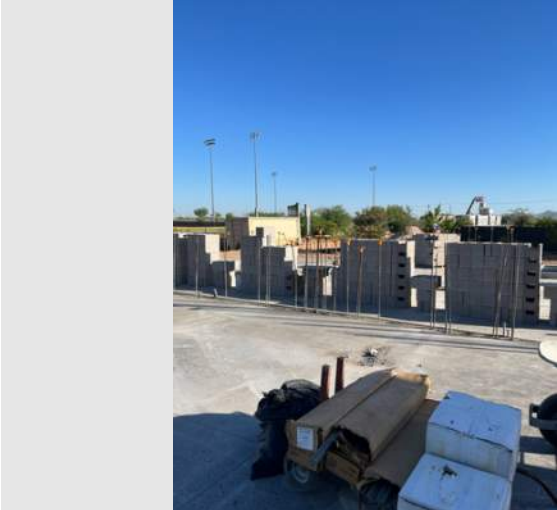

Description

Bldg. block spreading in progress.

Taken Date

06/14/2023 at 07:09 am

Uploaded By

Carlos Peralta

Upload Date

06/14/2023 at 07:09 am

File Name

F487F21E-8246-45D0-B54B-079C...



Description

East entry asphalt placement in progress.

Taken Date

06/14/2023 at 09:22 am

Uploaded By

Carlos Peralta

Upload Date

06/14/2023 at 09:22 am

File Name

79630A27-FC4C-4CE7-8C67-325...



Description

Door frames in place.

Taken Date

06/14/2023 at 07:09 am

Uploaded By

Carlos Peralta

Upload Date

06/14/2023 at 07:10 am

File Name

44CDCFB5-DDBB-4A6C-99E0-586...



Description

Bldg. slab complete and control joints saw cutting in progress.

Taken Date

06/09/2023 at 12:56 pm

Uploaded By


Saen Framjee

Upload Date

06/09/2023 at 01:58 pm

File Name

[8BDC9CDE-2699-4A25-90E7-92A...](#)

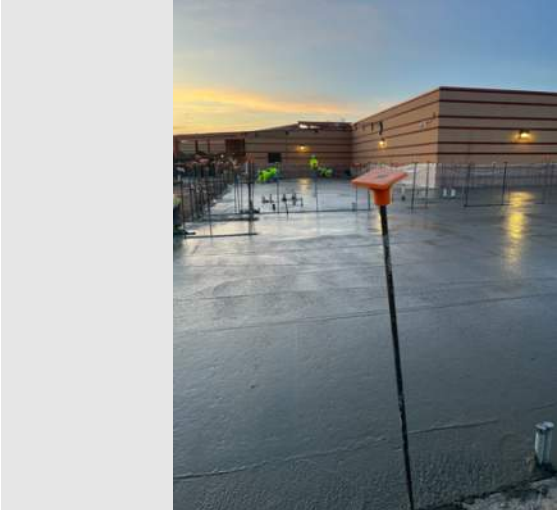

Description

Finishers on site.

Taken Date

06/09/2023 at 05:16 am

Uploaded By

Carlos Peralta

Upload Date

06/09/2023 at 05:17 am

File Name

[FFA656D2-15CE-429E-951C-FC84...](#)



Description

West side stairwell slab.

Taken Date

06/09/2023 at 05:16 am

Uploaded By


Carlos Peralta

Upload Date

06/09/2023 at 05:28 am

File Name

[085F7598-B076-4152-A425-5414...](#)

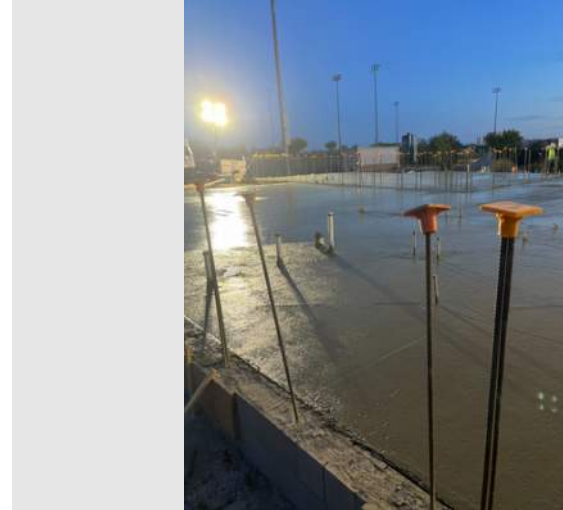

Description

2:00 AM slab concrete pour CJS

Taken Date

06/09/2023 at 04:59 am

Uploaded By


Carlos Peralta

Upload Date

06/09/2023 at 05:22 am

File Name

[AC77B189-8D19-4954-84A7-352...](#)

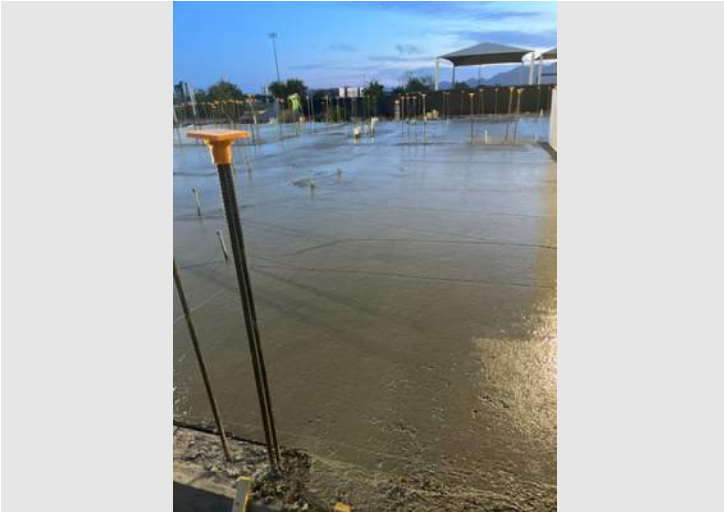

Description

Slab concrete pour 95 Yards.

Taken Date

06/09/2023 at 04:59 am

Uploaded By

Carlos Peralta

Upload Date

06/09/2023 at 05:28 am

File Name

[CCF8B6EE-4D1A-4ED5-9FBE-DF8...](#)



Description

Building B Pad With Vapor Barrier and Soil Poison installed. ready for concrete

Taken Date

06/08/2023 at 02:51 pm

Uploaded By

Saen Framjee

Upload Date

06/09/2023 at 09:25 am

File Name

[0E406AC2-C553-4466-AF7A-1499...](#)



Description

Asphalt completed

Taken Date

06/08/2023 at 02:52 pm

Uploaded By

Saen Framjee

Upload Date

06/09/2023 at 09:25 am

File Name

[D436B2AC-5F4C-4F47-908E-C72...](#)



Description

Vapor Barrier.

Taken Date

06/08/2023 at 01:25 pm

Uploaded By

Carlos Peralta

Upload Date

06/08/2023 at 01:26 pm

File Name

[2DB6E311-91A0-4D6A-8CDC-31B...](#)



Description

Vapor barrier installed.

Taken Date

06/08/2023 at 01:25 pm

Uploaded By

Carlos Peralta

Upload Date

06/08/2023 at 01:35 pm

File Name

[CC270A37-3715-4020-906C-31C...](#)



Description

Water test at parking lot.

Taken Date

06/08/2023 at 08:46 am

Uploaded By


Carlos Peralta

Upload Date

06/08/2023 at 08:46 am

File Name

[FA7319CA-E3A9-411A-B506-021E...](#)

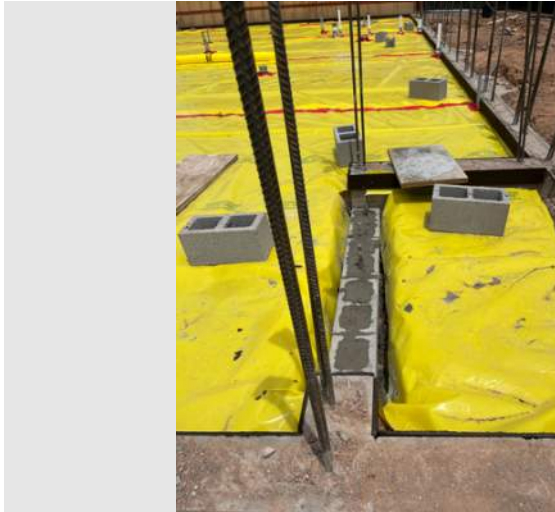

Description

CMU Block install over door frames.

Taken Date

06/08/2023 at 01:25 pm

Uploaded By

Carlos Peralta

Upload Date

06/08/2023 at 01:40 pm

File Name

[0A2124AE-0B76-410B-9FCB-901...](#)



Description

Washout tub on site deliver

Taken Date

06/08/2023 at 08:46 am

Uploaded By


Carlos Peralta

Upload Date

06/08/2023 at 08:47 am

File Name

[273A3BB0-D2BF-46E5-8414-669...](#)

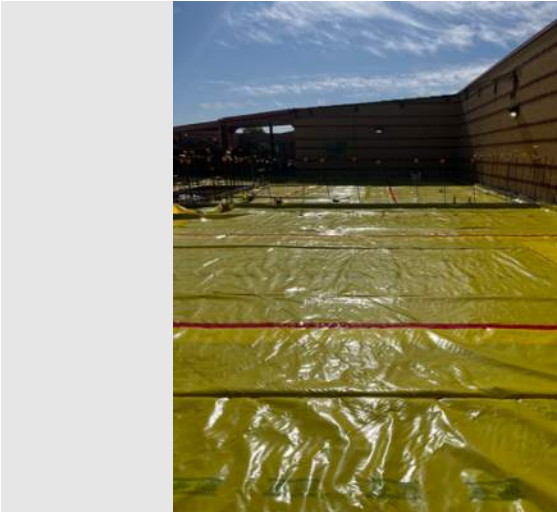

Description

Vapor barrier install complete.

Taken Date

06/06/2023 at 08:32 am

Uploaded By

Carlos Peralta

Upload Date

06/06/2023 at 10:52 am

File Name

99A303FF-60DB-418B-AB45-0DA...



Description

East side.

Taken Date

06/06/2023 at 07:29 am

Uploaded By


Carlos Peralta

Upload Date

06/06/2023 at 07:29 am

File Name

61EEDC0D-3D1B-480A-9DCA-0A3...

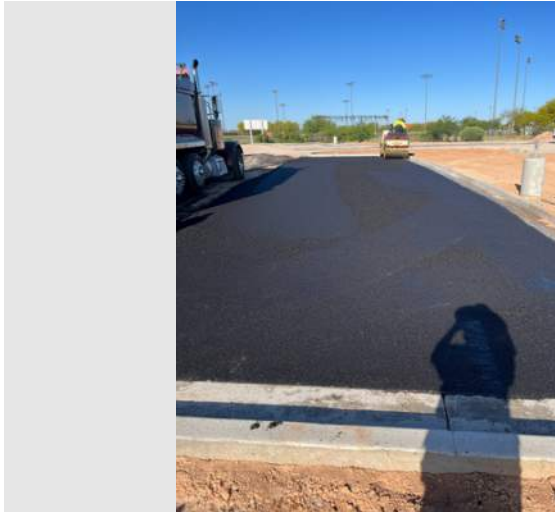

Description

Asphalt install in place parking lot.

Taken Date

06/06/2023 at 07:29 am

Uploaded By

Carlos Peralta

Upload Date

06/06/2023 at 07:29 am

File Name

3A57857A-7723-49B7-8635-2F22...



Description

SWPPP in place at dirt mountain on the west side.

Taken Date

06/05/2023 at 09:10 am

Uploaded By

Carlos Peralta

Upload Date

06/05/2023 at 12:46 pm

File Name

D40ED923-98E1-4CE9-BF9B-B36...



Description

Building B Ready for Concrete

Taken Date

06/02/2023 at 12:15 pm

Uploaded By

Saen Framjee

Upload Date

06/02/2023 at 01:31 pm

File Name

[DEBF2E43-AE0A-407E-A7FE-CFE1...](#)



Description

Parking lot ready for asphalt

Taken Date

06/02/2023 at 12:14 pm

Uploaded By

Saen Framjee

Upload Date

06/02/2023 at 01:31 pm

File Name

[8625FBC7-5D4D-48C4-908B-C9A...](#)



Description

Building B being prepped for Concrete

Taken Date

06/02/2023 at 12:15 pm

Uploaded By

Saen Framjee

Upload Date

06/02/2023 at 01:31 pm

File Name

[77B8A6C2-48B9-4326-988C-794...](#)



Description

Arial of parking lot with AB ready for asphalt

Taken Date

06/02/2023 at 12:14 pm

Uploaded By

Saen Framjee

Upload Date

06/02/2023 at 01:31 pm

File Name

[F07E8C6B-F274-41C9-AB69-0CE5...](#)



Description

Underground plumbing West bathroom

Taken Date

06/02/2023 at 06:44 am

Uploaded By

Carlos Peralta

Upload Date

06/02/2023 at 06:46 am

File Name

[3B1B0796-FE5F-4BEB-A382-D62...](#)



Description

AB Bldg.. B Compaction to follow.

Taken Date

06/01/2023 at 06:37 am

Uploaded By

Carlos Peralta

Upload Date

06/01/2023 at 06:50 am

File Name

[37064989-869F-411C-9A0F-A67C...](#)



Description

Conveyer belt Spreading AB bldg.B

Taken Date

06/01/2023 at 06:37 am

Uploaded By

Carlos Peralta

Upload Date

06/01/2023 at 06:44 am

File Name

[18606E2A-2B5F-4798-96E6-C15A...](#)

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Attachments:

Item/s
1. None
